

GroupID-PA1 Weekly Scrum Meeting Minutes

Section 1: Process Overview

Process methodology: RUP + Scrum.

RUP phases applied in PA1:

- Inception: form the group, choose the topic, and choose FIFA.com and Chess.com as the two products.
- Elaboration: analyze users, contexts, HCI concepts, risks, and screen/source evidence.
- Construction: write ProductResearch, PotentialSolutions, PeerReview, and WeeklyReport.
- Transition: export PDFs, validate the ZIP, and prepare the Moodle submission.

Scrum process:

- One sprint is fixed for 2 weeks, corresponding with PA1.
- Sprint 1 contains four meetings: Sprint Planning, Weekly Scrum 1, Weekly Scrum 2, and Sprint Review and Retrospective.

Templates used:

- Weekly scrum meeting minutes template.
- Sprint planning meeting minutes template.
- Sprint review meeting minutes template.

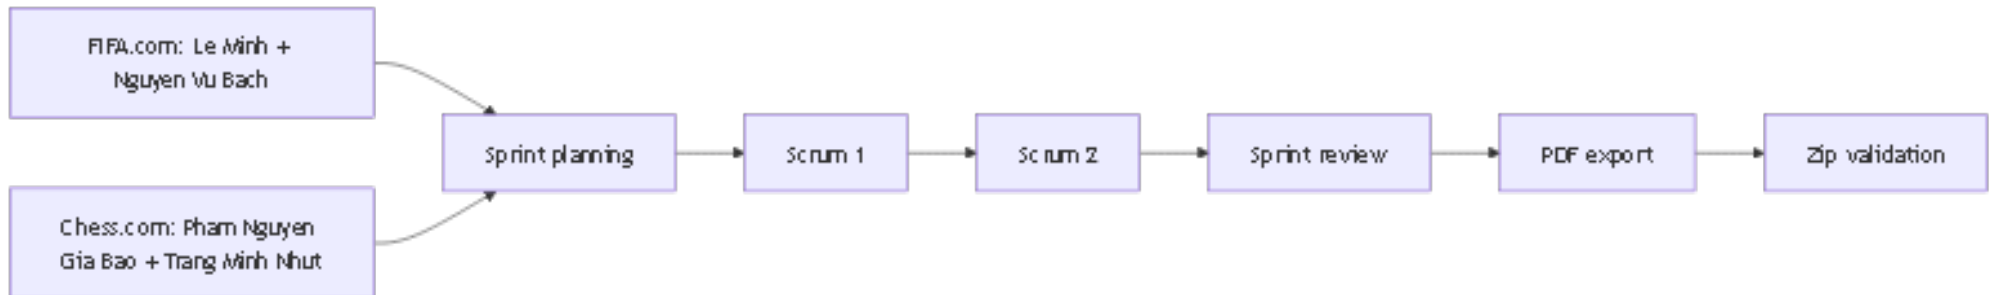


Diagram WR-D1. Sprint 1 process from planning through two scrums, review, export, and validation.

Section 2: Google Docs and Drive Structure

Resource	Link or artifact
Weekly Scrum Google Docs link	TODO
Sprint Planning Google Docs link	TODO
Sprint Review Google Docs link	TODO
Google Drive README link	TODO
GitHub repo link	https://github.com/jerrylemin/PA1-TKGD
Moodle zip artifact name	GroupID-PA1.zip

The required Drive folder structure is documented in docs/google_drive_readme_template.md.

Section 3: Team roster

Member	Student ID	Role	Main contribution
Le Minh	21127645	Project Coordinator, Integration Lead, PeerReview Lead, WeeklyReport Lead, Final Packaging Lead	Coordinated scope, integrated final reports, led PeerReview and WeeklyReport evidence, ran final PDF and zip packaging QA.
Nguyen Vu Bach	21127224	FIFA.com Research Lead, FIFA Screenshot Evidence Lead, ProductResearch Co-Lead	Researched FIFA.com, collected official sources, captured and annotated FIFA evidence, and wrote FIFA HCI findings.
Pham Nguyen Gia Bao	20127119	Chess.com Research Lead, Chess.com Screenshot Evidence Lead, ProductResearch Co-Lead	Researched Chess.com, collected official sources, captured and annotated Chess.com evidence, and wrote Chess.com HCI findings.
Trang Minh Nhut	22127318	HCI Analysis Lead, PotentialSolutions Lead, Visual QA Lead	Mapped HCI concepts, led PotentialSolutions, checked figure captions, and verified drawback-to-solution consistency.

Section 4: Meeting schedule

Meeting	Date	Time
Sprint Planning	2026-06-10	20:00 to 20:45
Weekly Scrum 1	2026-06-14	20:00 to 20:30
Weekly Scrum 2	2026-06-19	20:00 to 20:30
Sprint Review and Retrospective	2026-06-22	20:00 to 20:50

Section 5: Sprint Planning Meeting Minutes

===== 10/06, Sprint 1, Sprint Planning =====

- Date: 2026-06-10.
- Time: 20:00 to 20:45.
- Team members present: Le Minh, Nguyen Vu Bach, Pham Nguyen Gia Bao, Trang Minh Nhut.
- Team members absent: None.
- Meeting objective: agree on the PA1 sprint objective, product scope, selected use-case slices, ownership, evidence rules, and acceptance criteria.

Sprint objective

Produce evidence-grounded PA1 reports for FIFA.com and Chess.com and package exactly four PDFs in GroupID-PA1.zip.

Product decisions

The team selected FIFA.com as a browse-first official football ecosystem and Chess.com as an action-first play-and-learning platform.

Priority tasks

Collect official sources; capture and annotate visible screens; write personas and use cases; map HCI findings to drawbacks and two solutions; rehearse; export and validate.

User stories or use-case parts selected for PA1

FIFA: match lookup, official story/ranking lookup, tickets, and FIFA+ handoff. Chess.com: start play, premove, Focus Mode, Game Review/Analysis, puzzles and lessons.

Task assignment by member

Le Minh: coordination, integration, PeerReview, WeeklyReport, packaging. Nguyen Vu Bach: FIFA research/evidence. Pham Nguyen Gia Bao: Chess.com research/evidence. Trang Minh Nhut: HCI mapping, solutions, visual QA.

Actions

Use official sources first; keep F-/C-prefixed IDs stable; annotate only visible UI; regenerate every derived artifact after source changes.

Summary of the meeting

The group locked the pair, owners, two-week sprint scope, evidence protocol, four deliverables, and exact ZIP acceptance rule.

Section 6: Weekly Scrum 1 Meeting Minutes

===== 14/06, Sprint 1 =====

- Date: 2026-06-14.
- Time: 20:00 to 20:30.
- Team members present: Le Minh, Nguyen Vu Bach, Pham Nguyen Gia Bao, Trang Minh Nhut.
- Team members absent: None.

Member	Completed tasks	To-do tasks	Issues/Obstacles
Le Minh	Prepared the report structure, PA1 checklist, deliverable folders, and PeerReview outline.	Integrate the two product sections and prepare the QA checklist.	Product integration depends on completed evidence tables and captions.
Nguyen Vu Bach	Collected official FIFA.com sources, captured screenshots, and drafted FIFA personas and use cases.	Complete FIFA HCI findings and the canonical drawback list.	Dynamic FIFA pages require careful selection of visible evidence.
Pham Nguyen Gia Bao	Collected official Chess.com sources, captured screenshots, and drafted Chess.com personas and use cases.	Complete Chess.com HCI findings and the canonical drawback list.	Some review features require account state, so official support evidence is needed.
Trang Minh Nhut	Prepared the HCI mapping template, reviewed screenshots, and created the solution structure.	Convert final drawbacks into two HCI-based solutions each and check captions.	The solution draft depends on stable drawback IDs from both product leads.

Le Minh

- Completed tasks: Prepared the report structure, PA1 checklist, deliverable folders, and PeerReview outline.
- To-do tasks: Integrate the two product sections and prepare the QA checklist.
- Issues/Obstacles: Product integration depends on completed evidence tables and captions.

Nguyen Vu Bach

- Completed tasks: Collected official FIFA.com sources, captured screenshots, and drafted FIFA personas and use cases.
- To-do tasks: Complete FIFA HCI findings and the canonical drawback list.

- Issues/Obstacles: Dynamic FIFA pages require careful selection of visible evidence.

Pham Nguyen Gia Bao

- Completed tasks: Collected official Chess.com sources, captured screenshots, and drafted Chess.com personas and use cases.
- To-do tasks: Complete Chess.com HCI findings and the canonical drawback list.
- Issues/Obstacles: Some review features require account state, so official support evidence is needed.

Trang Minh Nhut

- Completed tasks: Prepared the HCI mapping template, reviewed screenshots, and created the solution structure.
- To-do tasks: Convert final drawbacks into two HCI-based solutions each and check captions.
- Issues/Obstacles: The solution draft depends on stable drawback IDs from both product leads.

Actions

Product leads will finish evidence tables and captions; Trang Minh Nhut will lock canonical drawback IDs before solution drafting; Le Minh will prepare integration QA.

Summary of the meeting

Source collection and initial use cases were on track; dynamic/login-only evidence remained the main limitation, so official support sources were retained where screens could not prove a claim.

Section 7: Weekly Scrum 2 Meeting Minutes

===== 19/06, Sprint 1 =====

- Date: 2026-06-19.
- Time: 20:00 to 20:30.
- Team members present: Le Minh, Nguyen Vu Bach, Pham Nguyen Gia Bao, Trang Minh Nhut.
- Team members absent: None.

Member	Completed tasks	To-do tasks	Issues/Obstacles
Le Minh	Integrated the draft reports, reviewed the PeerReview script, and checked filenames and ZIP requirements.	Finalize WeeklyReport, regenerate artifacts, and run the strict draft validator.	All unsupported readiness language must be removed while blockers remain.
Nguyen Vu Bach	Finished the FIFA.com overview, use cases, figures, benefits, drawbacks, and findings.	Review the regenerated ProductResearch PDF and its evidence captions.	Several FIFA claims rely on official sources rather than a visible captured state.
Pham Nguyen Gia Bao	Finished the Chess.com overview, use cases, figures, benefits, drawbacks, and findings.	Review ProductResearch and PotentialSolutions after regeneration.	The feature breadth can make the analysis too broad or generic.
Trang Minh Nhut	Completed the drawback-solution matrix, impact-effort table, rollout plan, and visual QA.	Check every canonical row, figure product prefix, and two-solution mapping.	Existing evidence rows contain semantic drift and must be regenerated from one map.

Le Minh

- Completed tasks: Integrated the draft reports, reviewed the PeerReview script, and checked filenames and ZIP requirements.
- To-do tasks: Finalize WeeklyReport, regenerate artifacts, and run the strict draft validator.

- Issues/Obstacles: All unsupported readiness language must be removed while blockers remain.

Nguyen Vu Bach

- Completed tasks: Finished the FIFA.com overview, use cases, figures, benefits, drawbacks, and findings.
- To-do tasks: Review the regenerated ProductResearch PDF and its evidence captions.
- Issues/Obstacles: Several FIFA claims rely on official sources rather than a visible captured state.

Pham Nguyen Gia Bao

- Completed tasks: Finished the Chess.com overview, use cases, figures, benefits, drawbacks, and findings.
- To-do tasks: Review ProductResearch and PotentialSolutions after regeneration.
- Issues/Obstacles: The feature breadth can make the analysis too broad or generic.

Trang Minh Nhut

- Completed tasks: Completed the drawback-solution matrix, impact-effort table, rollout plan, and visual QA.
- To-do tasks: Check every canonical row, figure product prefix, and two-solution mapping.
- Issues/Obstacles: Existing evidence rows contain semantic drift and must be regenerated from one map.

Actions

Correct the canonical evidence table, review all captions, remove unsupported readiness claims, regenerate PDFs/ZIP, and run PDF extraction plus strict draft validation.

Summary of the meeting

All report bodies were substantially complete; the remaining work was semantic traceability, honest blocker handling, export quality, and package validation.

Section 8: Sprint Review and Retrospective Meeting Minutes

===== 22/06, Sprint 1, Sprint Review and Retrospective =====

- Date: 2026-06-22.
- Time: 20:00 to 20:50.
- Team members present: Le Minh, Nguyen Vu Bach, Pham Nguyen Gia Bao, Trang Minh Nhut.
- Team members absent: None.
- Meeting objective: inspect the PA1 increment, review process outcomes, agree corrective actions, and decide the final draft packaging state.

What went well

The product pair, ownership, official-source protocol, personas, ten detailed use cases, annotated evidence, and balanced workload were completed consistently.

What went wrong

The first WeeklyReport was not in the strict process template, and one PotentialSolutions evidence table drifted from the canonical drawback meanings.

What problems occurred

Some dynamic/login-only states could not be captured; report tables became dense; GroupID and real classroom feedback were unavailable.

What caused the problems

The generator had duplicated mappings and hard-coded readiness assumptions, and validation checked ID presence rather than semantic relationships.

What the team will do differently in the next sprint

Centralize configuration and canonical mappings first, validate one vertical slice before duplication, and collect real feedback immediately after presentation.

Lessons learned

Visual polish cannot compensate for weak traceability or missing process evidence; final readiness must be gated by real identifiers, authentic feedback, extracted PDF text, and exact package contents.

Final PA1 packaging decision

Generate a READY DRAFT package with exactly four PDFs in GroupID-PA1.zip. Do not claim READY FINAL while GroupID or real peer feedback remains pending.

Actions

Le Minh runs the build and validators; Nguyen Vu Bach and Pham Nguyen Gia Bao review product evidence; Trang Minh Nhut rechecks canonical traceability; the team fills real feedback and group ID before final mode.

Summary of the meeting

The increment is acceptable as a validated draft after strict fixes, with two explicit external-information blockers remaining for final submission.

Section 9: Workload matrix

Equal ownership explanation: each member contributes research, writing, review, and final QA; website ownership is split two people per product, producing an equal quarter share per member.

Member	Website ownership	Research	Writing	Review	Final QA	Contribution
Le Minh	FIFA.com	Yes	Yes	Yes	Yes	25%
Nguyen Vu Bach	FIFA.com	Yes	Yes	Yes	Yes	25%
Pham Nguyen Gia Bao	Chess.com	Yes	Yes	Yes	Yes	25%
Trang Minh Nhut	Chess.com	Yes	Yes	Yes	Yes	25%

Section 10: Final submission checklist

Deliverable	Expected filename	Acceptance status
ProductResearch PDF	GroupID-PA1-ProductResearch.pdf	Contains FIFA.com and Chess.com evidence, figures, personas, use cases, HCI findings, references, and strict context labels.

Deliverable	Expected filename	Acceptance status
PotentialSolutions PDF	GroupID-PA1-PotentialSolutions.pdf	Contains drawback-to-solution mapping, solution details, priority/effort rationale, rollout plan, and solution figures.
PeerReview PDF	GroupID-PA1-PeerReview.pdf	Contains seven-minute script, slide plan, internal rehearsal feedback, and real owner names.
WeeklyReport PDF	GroupID-PA1-WeeklyReport.pdf	Contains real roster, planned dates, sprint planning, two per-member scrum records, sprint review, workload matrix, and checklist.
Submission package	GroupID-PA1.zip	Contains exactly the four final PDFs at top level.
