

PROJECT ASSIGNMENT 2

Group10-PA2 Weekly Report

Reconstructed three-week RUP + Scrum project process

FIFA.com and Chess.com

Course	CSC13112 - UI/UX Design, FIT-HCMUS
Group	Group10
Team	Le Minh (21127645); Nguyen Vu Bach (21127224); Pham Nguyen Gia Bao (20127119); Trang Minh Nhut (22127318)
Scope	Reconstructed three-week RUP + Scrum project process

Contents

Contents	2
1. Process Overview	4
2. Meeting Conduct and Cross-Report Decisions	4
3. Team Roster and Three-Week Schedule	5
4. Sprint Planning	8
4.1 Sprint Planning Meeting	8
5. Week 1 Scrum	11
5.1 Weekly Scrum - Week 1	11
6. Week 2 Scrum	13
6.1 Simulated Brainstorming Session	13
6.2 Weekly Scrum - Week 2	14
7. Week 3 Scrum	16
7.1 Weekly Scrum - Week 3	16
8. Sprint Review and Retrospective	18
8.1 Sprint Review and Retrospective	18
9. Workload Summary	19
10. Acceptance Checklist	22
11. Submission Status	23
12. Continuity with PA1	23

Process Flow	23
Practical Difficulties and Lessons Learned	24

1. Process Overview

Disclosure: This report documents a reconstructed three-week project process prepared for course reporting.

The process combines RUP phases with Scrum cadence: Inception establishes PA1 continuity and evidence rules; Elaboration defines simulated-study protocol, synthesis, and alternatives; Construction produces proposal, UML, use cases, traceability, and document builds; Transition performs visual QA and packaging.

Reconstructed project record: Dates, meetings, attendance, workload, and progress below are reconstructed or simulated project records; they are not presented as contemporaneous records.

2. Meeting Conduct and Cross-Report Decisions

Rule	Application
Evidence before claim	Screen states prove interface state; PA1 findings remain inherited; simulated study remains labeled; design implications remain inference.
Cross-report IDs	Participant, session, finding, cluster, problem, concept, recommendation, use case, and PA3 target IDs stay stable.
No unrecorded media	Structured notes only; no external communication references.
Decision control	Status Dashboard and Beginner Review Preset are recommendations; remaining alternatives stay in PA3 parallel prototyping.
Evidence validation	The PA1 lesson on wrong interface states becomes a PA2 validation gate for every figure and claim.

3. Team Roster and Three-Week Schedule

Record 1

Member	Le Minh
Primary ownership	Coordination, integration, traceability, packaging, Weekly Report
Research	Protocol integration
Writing	Weekly and cross-report sections
Review	Traceability and acceptance
Presentation / packaging	Package and submission

Record 2

Member	Nguyen Vu Bach
Primary ownership	FIFA research, simulated sessions, findings, proposal, use cases
Research	FIFA tasks/sessions
Writing	FIFA modules
Review	FIFA source/claim review
Presentation / packaging	FIFA presentation

Record 3

Member	Pham Nguyen Gia Bao
Primary ownership	Chess research, simulated sessions, findings, proposal, use cases
Research	Chess tasks/sessions
Writing	Chess modules
Review	Chess source/claim review
Presentation / packaging	Chess presentation

Record 4

Member	Trang Minh Nhut
Primary ownership	Brainstorming, affinity, prioritization, HCI mapping, diagrams, visual QA
Research	Synthesis protocol
Writing	Analysis and HCI mapping
Review	Diagram and layout review
Presentation / packaging	Visual consistency

Record 1

Week	1
Dates	14-18 Jul 2026
RUP focus	Inception / early Elaboration
Scrum goal	Scope, PA1 continuity, evidence audit, research plan, simulated session design, walkthrough
Main outputs	Protocol, participants, session records, screen-evidence boundary

Record 2

Week	2
Dates	20-24 Jul 2026
RUP focus	Elaboration
Scrum goal	Synthetic synthesis, brainstorming, affinity, voting, prioritization, tough problems, alternatives
Main outputs	72 notes, clusters, votes, weighted problems, six alternatives

Record 3

Week	3
Dates	27-30 Jul 2026
RUP focus	Construction / Transition
Scrum goal	Proposal, UML, use cases, traceability, QA, packaging
Main outputs	Six revised reports, internal design QA Peer Review, and six-PDF package

4. Sprint Planning

4.1 Sprint Planning Meeting

Field	Record
Record type	Reconstructed project record / Simulated meeting record
Date	14 Jul 2026
Time	20:00-20:50
Present	Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut
Absent	None
Objective	Translate PA2 rubric into a three-week backlog while preserving PA1 continuity.
Topics	Two products; PA1 drawbacks; evidence boundary; simulated-study labels; report ownership; definition of done.
Decisions	Keep FIFA and Chess; use three methods; label every synthetic record; label Peer Review as internal/simulated design QA; require traceability and page-render QA.
Actions	Le builds traceability skeleton; Bach audits FIFA; Bao audits Chess; Nhut maps lecture concepts and visual rules.
Summary	The team accepts one integrated sprint with weekly checkpoints and a final transition gate.

Record 1

Backlog item	PA1 continuity and screen-evidence audit
Owner	Le + Bach + Bao
Acceptance condition	Every high-level claim has a source label
Week	1

Record 2

Backlog item	12 simulated profiles/sessions/note sheets
Owner	Bach + Bao
Acceptance condition	IDs and metrics trace one-to-one
Week	1

Record 3

Backlog item	72 notes, affinity, votes, prioritization
Owner	Nhut
Acceptance condition	36 notes per product; 24 votes per product
Week	2

Record 4

Backlog item	Six alternatives and weighted comparison
Owner	Bach + Bao
Acceptance condition	All required evaluation fields and PA3 plan
Week	2

Record 5

Backlog item	12 detailed use cases and UML
Owner	Bach + Bao + Nhut
Acceptance condition	Six per product; include/extend; edge cases
Week	3

Record 6

Backlog item	Build, render, traceability, QA, ZIP
Owner	Le + Nhut
Acceptance condition	Six PDFs only; Peer Review identifies artifact, severity, recommendation, action, and result
Week	3

5. Week 1 Scrum

5.1 Weekly Scrum - Week 1

Field	Record
Record type	Reconstructed project record / Simulated meeting record
Date	17 Jul 2026
Time	20:00-20:30
Present	Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut
Absent	None
Objective	Check scope, evidence audit, protocol, simulated-session design, and walkthrough progress.
Topics	PA1 continuity; screen inventory; task lists; participant balance; evidence-state mistakes.
Decisions	Retain 12 scenario profiles across two products; every note sheet must contain limitation and PA3 question.
Actions	Finish final two sessions on 18 Jul; map each result to one note sheet; flag partner/engine claims as untested.
Summary	Week 1 establishes a bounded research artifact without representing synthetic sessions as real research.

Record 1

Member	Le Minh
Completed	Rubric matrix, continuity chain, source-label rules
Next	Integrate task/result IDs
Obstacle	Legacy files use provisional wording

Record 2

Member	Nguyen Vu Bach
Completed	FIFA walkthrough, six profiles, first four session records
Next	Finish FIFA notes and findings
Obstacle	Ticket feed and partner state unavailable

Record 3

Member	Pham Nguyen Gia Bao
Completed	Chess walkthrough, six profiles, first four session records
Next	Finish Chess notes and findings
Obstacle	No completed engine review evidence

Record 4

Member	Trang Minh Nhut
Completed	Lecture mapping and evidence visual audit
Next	Model legends and layout rules
Obstacle	Long captures require readable splits

6. Week 2 Scrum

6.1 Simulated Brainstorming Session

Field	Record
Record type	Reconstructed project record / Simulated meeting record
Date	22 Jul 2026
Time	19:30-20:45
Present	Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut
Absent	None
Objective	Cluster 72 atomic notes and establish product priorities.
Topics	Silent generation; round-robin; duplicate merging; cluster naming; simulated voting; weighted scoring.
Decisions	FIFA prioritizes status and handoff confidence; Chess consolidates entry, explanation, and continuation into guided beginner review.
Actions	Nhut maintains clusters/votes; Bach and Bao write problem profiles; Le checks traceability.
Summary	The synthetic workshop produces design hypotheses and is not contemporaneous meeting evidence.

6.2 Weekly Scrum - Week 2

Field	Record
Record type	Reconstructed project record / Simulated meeting record
Date	24 Jul 2026
Time	20:00-20:30
Present	Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut
Absent	None
Objective	Review synthesis, tough problems, and six alternatives.
Topics	Affinity counts; vote totals; weighted rationale; product boundary; PA3 parallel prototypes.
Decisions	Select TP-FIFA and TP-CHESS; recommend F-A1 and C-A1 while retaining four alternatives.
Actions	Draft comparison formula, accessibility/privacy/data/recovery fields, and PA3 test measures.
Summary	Week 2 converts evidence and synthetic patterns into explicit, testable design directions.

Record 1

Member	Le Minh
Completed	Traceability through tough problems
Next	Integrate recommendations and use cases
Obstacle	Cross-report terminology drift

Record 2

Member	Nguyen Vu Bach
Completed	FIFA findings, clusters, alternatives
Next	FIFA proposal and six use cases
Obstacle	State taxonomy depends on governed data

Record 3

Member	Pham Nguyen Gia Bao
Completed	Chess findings, clusters, alternatives
Next	Chess proposal and six use cases
Obstacle	Explanation quality requires PA3 validation

Record 4

Member	Trang Minh Nhut
Completed	72-note affinity, vote tables, HCI dimensions
Next	UML and visual QA
Obstacle	Wide tables require landscape sections

7. Week 3 Scrum

7.1 Weekly Scrum - Week 3

Field	Record
Record type	Reconstructed project record / Simulated meeting record
Date	29 Jul 2026
Time	20:00-20:30
Present	Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut
Absent	None
Objective	Close proposal, UML, detailed use cases, traceability, and build defects.
Topics	Weighted recommendations; include/extend direction; use-case numbering; edge cases; source labels; layout.
Decisions	Use 12 exact use cases; restart every main flow at 1; preserve advanced Chess depth by disclosure; never infer FIFA partner completion.
Actions	Build revised DOCX/PDF, render every page, correct layout and banned text, prepare six-PDF ZIP.
Summary	Week 3 moves from content completion to evidence-backed transition QA.

Record 1

Member	Le Minh
Completed	Proposal integration, traceability CSV, weekly draft
Next	Package and final acceptance
Obstacle	TOC page numbers require final render

Record 2

Member	Nguyen Vu Bach
Completed	FIFA proposal and use cases
Next	Cross-check FIFA edge cases
Obstacle	Partner failure cannot be live-tested

Record 3

Member	Pham Nguyen Gia Bao
Completed	Chess proposal and use cases
Next	Cross-check Chess edge cases
Obstacle	Engine unavailable path is scenario-based

Record 4

Member	Trang Minh Nhut
Completed	UML, diagrams, landscape tables
Next	All-page visual QA
Obstacle	Dense note and traceability tables

8. Sprint Review and Retrospective

8.1 Sprint Review and Retrospective

Field	Record
Record type	Reconstructed project record / Simulated meeting record
Date	30 Jul 2026
Time	20:00-20:50
Present	Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut
Absent	None
Objective	Inspect final artifacts against rubric and record improvements for PA3.
Topics	Research completeness; analysis trace; recommendation logic; UML/use cases; simulated labels; page render; package contents.
Decisions	Accept five revised reports when QA passes; publish Peer Review as internal/simulated design QA; carry all unverified benefits to PA3 targets.
Actions	Le completes package; Nhut records QA; Bach/Bao verify product-specific claims and edge cases.
Summary	The sprint review closes PA2 reporting and leaves PA3 with explicit validation questions rather than synthetic certainty.

Field	Record
What worked	Stable IDs, source labels, product separation, and one evidence-to-use-case chain reduced ambiguity.

Field	Record
What did not work	Legacy documents were too provisional, too short in analysis/weekly reporting, and lacked traceable synthetic records.
Improvement	Validate state before capture, keep synthetic/observed evidence distinct, and prototype alternatives in parallel before commitment.
PA3 carryover	Observe users, test prototypes, replace synthetic expectations with measured task evidence, and retain accessibility/privacy/recovery gates.

9. Workload Summary

Record 1

Member	Le Minh
Research	Protocol integration
Writing	Weekly, traceability, integration
Review	Acceptance and cross-report consistency
Presentation / packaging	Packaging
Reconstructed hours	27
Status	Complete

Record 2

Member	Nguyen Vu Bach
Research	FIFA walkthrough/sessions
Writing	FIFA findings, proposal, use cases
Review	FIFA claims and edge cases
Presentation / packaging	FIFA report support
Reconstructed hours	26
Status	Complete

Record 3

Member	Pham Nguyen Gia Bao
Research	Chess walkthrough/sessions
Writing	Chess findings, proposal, use cases
Review	Chess claims and edge cases
Presentation / packaging	Chess report support
Reconstructed hours	26
Status	Complete

Record 4

Member	Trang Minh Nhut
Research	Synthesis protocol
Writing	Affinity, HCI mapping
Review	Diagram/layout consistency
Presentation / packaging	Visual QA
Reconstructed hours	25
Status	Complete

Reconstructed project record: Hours are reconstructed workload history for balanced course reporting, not time-tracker evidence.

10. Acceptance Checklist

Acceptance item	Evidence	Status
User Research	12 profiles, 12 sessions, 12 note sheets, metrics, 4 personas, 8 models, findings	Complete
User Analysis	72 notes, 13 clusters, voting, weighted prioritization, two tough problems	Complete
Project Proposal	Six alternatives, formula, two recommendations, PA3 parallel plan	Complete
Use Case Document	Two UML diagrams, 12 use cases, required edge cases	Complete
Peer Review	Internal/simulated design QA review with traceable actions	Revised for design QA
Weekly Report	Three weeks, meetings, scrums, workload, disclosure	Complete
QA and package	Selectable text, TOC, renders, CSVs, labels, traceability, six-PDF ZIP	Transition gate

11. Submission Status

Artifact	Owner	Submission state
Group10-PA2-UserResearch.pdf	Bach + Bao + Le	Ready after final QA
Group10-PA2-UserAnalysis.pdf	Nhut + Le	Ready after final QA
Group10-PA2-ProjectProposal.pdf	Bach + Bao	Ready after final QA
Group10-PA2-UseCaseDocument.pdf	Bach + Bao + Nhut	Ready after final QA
Group10-PA2-PeerReview.pdf	Group10 design QA	Revised for design QA
Group10-PA2-WeeklyReport.pdf	Le Minh	Ready after final QA

12. Continuity with PA1

- The same FIFA.com and Chess.com product pair continues.
- The same four members and responsibilities continue.
- PA1 drawbacks become PA2 tough problems.
- PA1 evidence rules become the PA2 research protocol.
- The PA1 lesson about screenshots showing the wrong state becomes the PA2 evidence-validation gate.

Process Flow

PA2 Three-Week Process

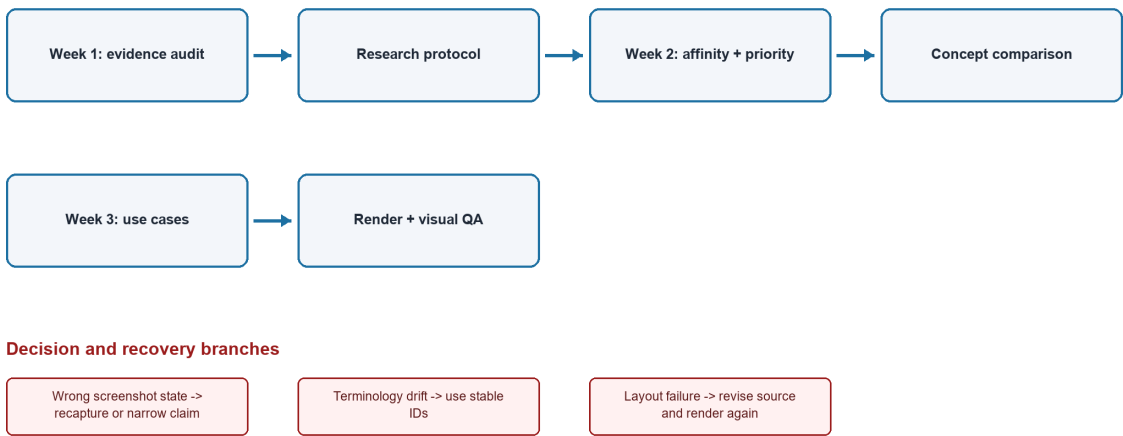


Figure WR-FLOW-01. Three-week PA2 process from evidence audit to all-page visual QA
Source: Weekly schedule, recovery gates, and final package
Related: 16.0

Practical Difficulties and Lessons Learned

Record 1

Practical difficulty	Ticket status and partner handoff changed across capture times.
How the group handled it	The team treated each screenshot as a dated state and avoided claiming a live outcome.
Lesson learned	Time-sensitive interface evidence needs a freshness boundary.
Impact on the final version	Final reports separate current, stale, unknown, and unavailable states.

Record 2

Practical difficulty	Terms from PA1 and PA2 drifted across reports.
How the group handled it	The team fixed stable names for problems, concepts, states, and use cases.
Lesson learned	Shared terms reduce broken traceability.
Impact on the final version	The final package uses the same FIFA and Chess labels in every report.
