

PROJECT ASSIGNMENT 2

Group10-PA2 Weekly Report

FIFA.com and Chess.com

Course	CSC13112 - UI/UX Design, FIT-HCMUS
Group	Group10
Team	Le Minh (21127645); Nguyen Vu Bach (21127224); Pham Nguyen Gia Bao (20127119); Trang Minh Nhut (22127318)

Contents

1. Process Overview	— 3
2. Meeting Conduct and Cross-Report Decisions	— 3
3. Team Roster and Three-Week Schedule	— 4
4. Sprint Planning	— 5
4.1 Sprint Planning Meeting	— 5
5. Week 1 Scrum	— 7
5.1 Weekly Scrum - Week 1	— 7
6. Week 2 Scrum	— 9
6.1 Simulated Brainstorming Session	— 9
6.2 Weekly Scrum - Week 2	— 10
7. Week 3 Scrum	— 12
7.1 Weekly Scrum - Week 3	— 12
8. Sprint Review and Retrospective	— 14
8.1 Sprint Review and Retrospective	— 14
9. Workload Summary	— 16
10. Acceptance Checklist	— 16
11. Submission Status	— 17
12. Continuity with PA1	— 18
13. RUP + Scrum Process Flow	— 18
14. Cross-report Lessons Applied	— 19

1. Process Overview

Disclosure: This report documents a reconstructed three-week project process prepared for course reporting.

The process combines RUP phases with Scrum cadence: Inception establishes PA1 continuity and evidence rules; Elaboration defines simulated-study protocol, synthesis, and alternatives; Construction produces proposal, UML, use cases, traceability, and document builds; Transition performs visual QA and packaging.

Reconstructed project record: Dates, meetings, attendance, workload, and progress below are reconstructed or simulated project records; they are not presented as contemporaneous records.

2. Meeting Conduct and Cross-Report Decisions

Rule	Application
Evidence before claim	Screen states prove interface state; PA1 findings remain inherited; simulated study remains labeled; design implications remain inference.
Cross-report IDs	Participant, session, finding, cluster, problem, concept, recommendation, use case, and PA3 target IDs stay stable.
No unrecorded media	Structured notes only; no external communication references.
Decision control	Status Dashboard and Beginner Review Preset are recommendations; remaining alternatives stay in PA3 parallel prototyping.
Evidence validation	The PA1 lesson on wrong interface states becomes a PA2 validation gate for every figure and claim.

3. Team Roster and Three-Week Schedule

Member	Primary ownership	Research	Writing	Review	Presentation / packaging
Le Minh	Coordination, integration, traceability, packaging, Weekly Report	Protocol integration	Weekly and cross-report sections	Traceability and acceptance	Presentation and submission packaging
Nguyen Vu Bach	FIFA research, simulated sessions, findings, proposal, use cases	FIFA tasks/sessions	FIFA modules	FIFA source/claim review	FIFA presentation
Pham Nguyen Gia Bao	Chess research, simulated sessions, findings, proposal, use cases	Chess tasks/sessions	Chess modules	Chess source/claim review	Chess presentation
Trang Minh Nhut	Brainstorming, affinity, prioritization, HCI mapping, diagrams, visual QA	Synthesis protocol	Analysis and HCI mapping	Diagram and layout review	Visual consistency
Week	Dates	RUP focus	Scrum goal		Main outputs
1	14-18 Jul 2026	Inception / early Elaboration	Scope, PA1 continuity, evidence audit, research plan, simulated session design, walkthrough		Protocol, participants, session records, screen-evidence boundary

Member	Primary ownership	Research	Writing	Review	Presentation / packaging
2	20-24 Jul 2026	Elaboration	Synthetic synthesis, brainstorming, affinity, voting, prioritization, tough problems, alternatives		72 notes, clusters, votes, weighted problems, six alternatives
3	27-30 Jul 2026	Construction / Transition	Proposal, UML, use cases, traceability, QA, packaging		Five revised DOCX reports and DOCX-only QA records

4. Sprint Planning

4.1 Sprint Planning Meeting

Field	Record
Record type	Reconstructed project record / Simulated meeting record
Date	14 Jul 2026
Time	20:00-20:50
Present	Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut
Absent	None
Objective	Translate PA2 rubric into a three-week backlog while preserving PA1 continuity.
Topics	Two products; PA1 drawbacks; evidence

Field		Record	
		boundary; simulated-study labels; report ownership; definition of done.	
Decisions		Keep FIFA and Chess; use three methods; label every synthetic record; label Peer Review as internal/simulated design QA; require traceability and page-render QA.	
Actions		Le builds traceability skeleton; Bach audits FIFA; Bao audits Chess; Nhut maps lecture concepts and visual rules.	
Summary		The team accepts one integrated sprint with weekly checkpoints and a final transition gate.	
Backlog item	Owner	Acceptance condition	Week
PA1 continuity and screen-evidence audit	Le + Bach + Bao	Every high-level claim has a source label	1
12 simulated profiles/sessions/note sheets	Bach + Bao	IDs and metrics trace one-to-one	1
72 notes, affinity, votes, prioritization	Nhut	36 notes per product; 24 votes per product	2
Six alternatives and weighted comparison	Bach + Bao	All required evaluation fields and PA3 plan	2
12 detailed use cases	Bach + Bao +	Six per product;	3

Field		Record	
and UML	Nhut	include/extend; edge cases	
Build, traceability, DOCX render QA, and submission review	Le + Nhut	Five DOCX files only; each opens and passes the DOCX checklist	3

5. Week 1 Scrum

5.1 Weekly Scrum - Week 1

Field		Record
Record type		Reconstructed project record / Simulated meeting record
Date		17 Jul 2026
Time		20:00-20:30
Present		Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut
Absent		None
Objective		Check scope, evidence audit, protocol, simulated-session design, and walkthrough progress.
Topics		PA1 continuity; screen inventory; task lists;

Field		Record	
		participant balance; evidence-state mistakes.	
Decisions		Retain 12 scenario profiles across two products; every note sheet must contain limitation and PA3 question.	
Actions		Finish final two sessions on 18 Jul; map each result to one note sheet; flag partner/engine claims as untested.	
Summary		Week 1 establishes a bounded research artifact without representing synthetic sessions as real research.	
Member	Completed	Next	Obstacle
Le Minh	Rubric matrix, continuity chain, source-label rules	Integrate task/result IDs	Legacy files use provisional wording
Nguyen Vu Bach	FIFA walkthrough, six profiles, first four session records	Finish FIFA notes and findings	Ticket feed and partner state unavailable
Pham Nguyen Gia Bao	Chess walkthrough, six profiles, first four session records	Finish Chess notes and findings	No completed engine review evidence
Trang Minh Nhut	Lecture mapping and evidence visual audit	Model legends and layout rules	Long captures require readable splits

6. Week 2 Scrum

6.1 Simulated Brainstorming Session

Field	Record
Record type	Reconstructed project record / Simulated meeting record
Date	22 Jul 2026
Time	19:30-20:45
Present	Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut
Absent	None
Objective	Cluster 72 atomic notes and establish product priorities.
Topics	Silent generation; round-robin; duplicate merging; cluster naming; simulated voting; weighted scoring.
Decisions	FIFA prioritizes status and handoff confidence; Chess consolidates entry, explanation, and continuation into guided beginner review.
Actions	Nhut maintains clusters/votes; Bach and Bao write problem profiles; Le checks traceability.
Summary	The synthetic workshop produces design

Field	Record
	hypotheses and is not contemporaneous meeting evidence.

6.2 Weekly Scrum - Week 2

Field	Record
Record type	Reconstructed project record / Simulated meeting record
Date	24 Jul 2026
Time	20:00-20:30
Present	Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut
Absent	None
Objective	Review synthesis, tough problems, and six alternatives.
Topics	Affinity counts; vote totals; weighted rationale; product boundary; PA3 parallel prototypes.
Decisions	Select TP-FIFA and TP-CHESS; recommend F-A1 and C-A1 while retaining four alternatives.
Actions	Draft comparison formula, accessibility/privacy/data/recovery fields, and PA3 test measures.

Field		Record	
Summary		Week 2 converts evidence and synthetic patterns into explicit, testable design directions.	
Member	Completed	Next	Obstacle
Le Minh	Traceability through tough problems	Integrate recommendations and use cases	Cross-report terminology drift
Nguyen Vu Bach	FIFA findings, clusters, alternatives	FIFA proposal and six use cases	State taxonomy depends on governed data
Pham Nguyen Gia Bao	Chess findings, clusters, alternatives	Chess proposal and six use cases	Explanation quality requires PA3 validation
Trang Minh Nhut	72-note affinity, vote tables, HCI dimensions	UML and visual QA	Wide tables require landscape sections

7. Week 3 Scrum

7.1 Weekly Scrum - Week 3

Field	Record
Record type	Reconstructed project record / Simulated meeting record
Date	29 Jul 2026

Field		Record	
Time		20:00-20:30	
Present		Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut	
Absent		None	
Objective		Close proposal, UML, detailed use cases, traceability, and build defects.	
Topics		Weighted recommendations; include/extend direction; use-case numbering; edge cases; source labels; layout.	
Decisions		Use 12 exact use cases; restart every main flow at 1; preserve advanced Chess depth by disclosure; never infer FIFA partner completion.	
Actions		Build the five revised DOCX files, inspect every rendered DOCX page, and correct layout or banned text.	
Summary		Week 3 moves from content completion to evidence-backed transition QA.	
Member	Completed	Next	Obstacle
Le Minh	Proposal integration, traceability CSV, weekly draft	DOCX set and final acceptance	TOC fields require a final DOCX update

Field		Record	
Nguyen Vu Bach	FIFA proposal and use cases	Cross-check FIFA edge cases	Partner failure cannot be live-tested
Pham Nguyen Gia Bao	Chess proposal and use cases	Cross-check Chess edge cases	Engine unavailable path is scenario-based
Trang Minh Nhut	UML, diagrams, landscape tables	All-page visual QA	Dense note and traceability tables

8. Sprint Review and Retrospective

8.1 Sprint Review and Retrospective

Field	Record
Record type	Reconstructed project record / Simulated meeting record
Date	30 Jul 2026
Time	20:00-20:50
Present	Le Minh; Nguyen Vu Bach; Pham Nguyen Gia Bao; Trang Minh Nhut
Absent	None
Objective	Inspect final artifacts against rubric and record

Field	Record
	improvements for PA3.
Topics	Research completeness; analysis trace; recommendation logic; UML/use cases; simulated labels; DOCX page render and acceptance checklist.
Decisions	Accept five revised reports when QA passes; publish Peer Review as internal/simulated design QA; carry all unverified benefits to PA3 targets.
Actions	Le completes the five-document set; Nhut records DOCX QA; Bach and Bao verify product-specific claims and edge cases.
Summary	The sprint review closes the five PA2 reports and leaves PA3 with explicit validation questions rather than synthetic certainty.
Field	Record
What went well	Stable IDs, source labels, and separate FIFA/Chess traces reduced ambiguity.
What went wrong	Some screenshots captured the wrong state, and long mobile pages became unreadable when reduced.
Problems encountered	Ticket and partner states changed; Chess analysis had several entry paths; affinity notes and use cases became dense.
Causes	Time-sensitive services, different mobile/desktop

Field	Record
	ordering, repeated terminology, and tables that tried to carry too much detail.
What we changed	We split long captures, moved raw records to appendices, separated empty/error/validation states, and gave each use case a unique visual.
Lessons learned	Validate the visible state before capture, preserve context during recovery, and split information at decision boundaries.
Actions for PA3	Test the Concierge branches and Beginner Review with representative users; measure interpretation, recovery, and continuation.

9. Workload Summary

Balanced contribution across four members

Member	Research	Writing	Review	Presentation / packaging
Le Minh	Protocol integration	Weekly report, traceability, integration	Acceptance and cross-report consistency	Submission structure and packaging
Nguyen Vu Bach	FIFA walkthrough and sessions	FIFA findings, proposal, and use cases	FIFA claims and edge cases	FIFA presentation support
Pham Nguyen	Chess walkthrough	Chess findings, proposal, and	Chess claims and edge	Chess presentation

Member	Research	Writing	Review	Presentation / packaging
Gia Bao	and sessions	use cases	cases	support
Trang Minh Nhut	Synthesis protocol	Affinity and HCI mapping	Diagram and layout consistency	Visual QA and presentation consistency

10. Acceptance Checklist

Acceptance item	Evidence	Status
User Research	12 profiles; six representative sessions; 12 detailed sheets in Appendix A; evidence figures; eight work models	Complete
User Analysis	14 representative notes; 72 raw notes in Appendix A; 13 clusters; vote visualization; weighted prioritization	Complete
Project Proposal	Six alternatives; detailed Guided Concierge; complete state and recovery matrix	Complete
Use Case Document	Two UML diagrams; 12 detailed use cases; 12 unique visuals; state reference	Complete
Weekly Report	Three weeks; RUP + Scrum; expanded retrospective; balanced contribution summary	Complete

11. Submission Status

Artifact	Owner	Submission state
Group10-PA2-UserResearch.docx	Bach + Bao + Le	Ready after DOCX QA
Group10-PA2-UserAnalysis.docx	Nhut + Le	Ready after DOCX QA
Group10-PA2-ProjectProposal.docx	Bach + Bao	Ready after DOCX QA
Group10-PA2-UseCaseDocument.docx	Bach + Bao + Nhut	Ready after DOCX QA
Group10-PA2-WeeklyReport.docx	Le Minh	Ready after DOCX QA

12. Continuity with PA1

- The same FIFA.com and Chess.com product pair continues.
- The same four members and responsibilities continue.
- PA1 drawbacks become PA2 tough problems.
- PA1 evidence rules become the PA2 research protocol.
- The PA1 lesson about screenshots showing the wrong state becomes the PA2 evidence-validation gate.

13. RUP + Scrum Process Flow

PA2 RUP + Scrum Delivery Loop

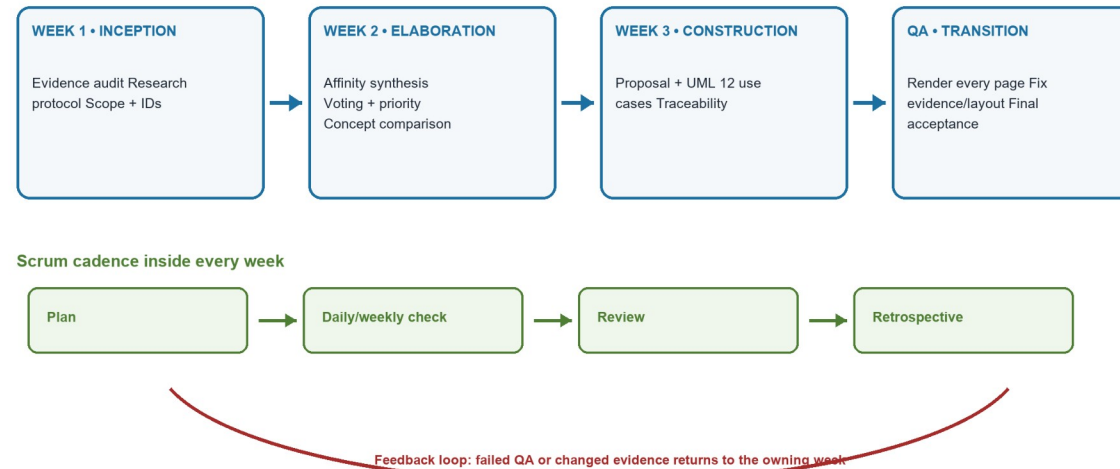


Figure WR-FLOW-01. RUP phases aligned to Week 1, Week 2, Week 3, and final QA, with Scrum cadence inside each week and a feedback loop to the owning phase.

14. Cross-report Lessons Applied

Practical difficulty	How the group handled it	Lesson learned	Impact on the final version
The first evidence crop showed a page footer instead of a ticket action.	The team reopened the full capture, selected the visible action region, and narrowed the caption to what the pixels prove.	Caption wording must be validated against the exact crop, not the source filename.	User Research now distinguishes later actions, pre-handoff state, and an unverified redirect.
Wide prioritization data created continuation pages with little content.	The team split FIFA and Chess candidates and combined criterion scores into a readable field.	Pagination is part of information architecture, especially for comparison tables.	The priority section is shorter and each product can be reviewed independently.
Early mockups used repeated boxes and generic labels.	The team added real tournament, match, party, status, timestamp, domain, board, move, lesson, and puzzle data.	A prototype must expose the decision and interaction, not merely name a component.	Guided Concierge and all 12 use-case visuals now demonstrate product-specific UI states.

Practical difficulty	How the group handled it	Lesson learned	Impact on the final version
Static contents drifted after sections moved and pages changed.	The team repaginated in Word and rebuilt each contents list from actual Heading 1-3 paragraphs.	Navigation must be verified after the final layout pass.	All five DOCX files have refreshed section order and page references.
A compact appendix still needed to retain all synthetic note fields at 14 pt.	The team moved note sheets to a landscape appendix with compact padding and one sheet per page.	Density should be solved with page geometry and grouping before reducing type size.	All 12 note sheets remain complete without two-page spillovers.
